


# Update on ISR DT Storage&Work Status

A.Benvenuti  
MU Week April 4<sup>th</sup> 2002

# ISR Chamber Tests Status

- Gas installation inside tunnel completed but no progress on outside gas shelter => still on pre-mixed bottles
- New set of trigger counters installed under the chamber operational => 53 Hz trigger rate (old trigger => 4 Hz)
- No progress on Ethernet + phone upgrade, yet another option (wireless hook up) obscures real issue => who pays
- MB2 chambers repaired (HV) but still noisy wires
- Legnaro scaler system would allow to make fast noise measurements on chamber stacks but fixes are difficult at the ISR
- List of Urgent items not shrinking.....

# Tasks at I3 Before DT Installation

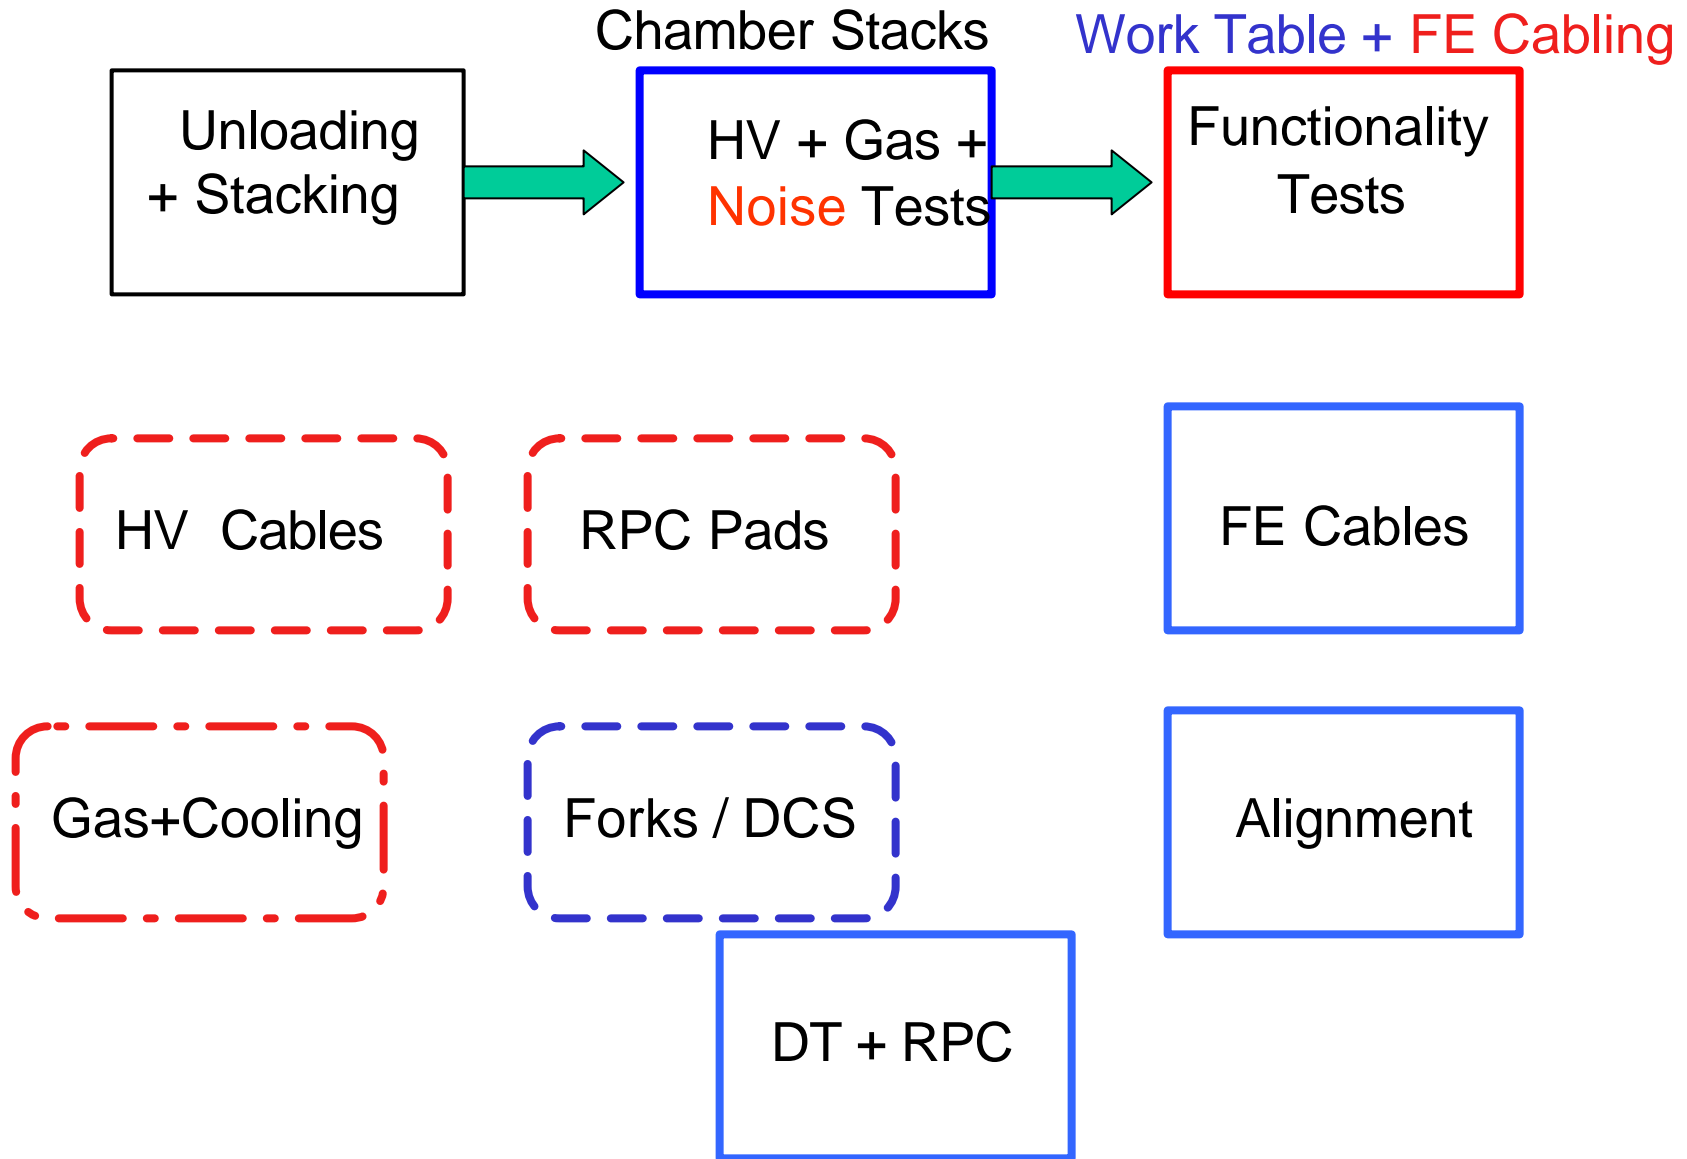

## Urgently Needed

- Final gas (water) connectors
- RPC docking pads (time consuming operation at ISR, should be done at sites)
- HV cables, still 8days away from definition ???
- Analysis programs, strategy (large volume of channels to look at)
- Standardization of QC parameters, definition of good chamber in terms of:
  - leak rate, dead channels, noisy channels,.....
- Chamber handling tools
- Second HV system.....
